
KVB Bridge Lighting

ID	% Compl	Task Mo	GS	Job Name	Task Name	Duration	Start	Finish	Predecessors	Responsi	Notifier	Crews	Equipment	Notes
1	**0%**		**JC**	**253309 - KVB Bridge Lightir**	**253309 - KVB Bridge Lighting**	**73 days**	**Tue 4/29/25**	**Mon 9/8/25**						
2	**0%**		**JC**	**253309 - KVB Bridge Lightir**	**Begin Pre-Con**	**1 day**	**Fri 5/23/25**	**Fri 5/23/25**						
3	0%		JC	253309 - KVB Bridge Lightin	PO Received	1 day	Fri 5/23/25	Fri 5/23/25						
4	**0%**		**JC**	**253309 - KVB Bridge Lightir**	**Material Procurement**	**49 days**	**Tue 4/29/25**	**Fri 7/25/25**						
5	0%		JC	253309 - KVB Bridge Lightin	Fixture Ship Date (Spots/Floods)	4 days	Fri 5/9/25	Wed 5/14/25						
6	0%		JC	253309 - KVB Bridge Lightin	Fixture Ship Date (Linear Fixtures)	3 days	Fri 5/30/25	Tue 6/3/25						
7	0%		JC	253309 - KVB Bridge Lightin	Cable & Drivers Ship Date	3 days	Fri 6/27/25	Tue 7/1/25						
8	0%		JC	253309 - KVB Bridge Lightin	DMX Controls Ship Date	2 days	Fri 6/27/25	Mon 6/30/25						
9	0%		JC	253309 - KVB Bridge Lightin	Dimming Controls Ship Date	2 days	Tue 4/29/25	Wed 4/30/25						
10	**0%**		**JC**	**253309 - KVB Bridge Lightir**	**Construction**	**39 days**	**Tue 6/10/25**	**Wed 8/13/25**						
11	0%		JC	253309 - KVB Bridge Lightin	North Side Arch	20 days	Tue 6/10/25	Mon 7/14/25						
12	0%		JC	253309 - KVB Bridge Lightin	South Side Arch	20 days	Mon 7/14/25	Wed 8/13/25						
13	0%		JC	253309 - KVB Bridge Lightin	North Side Beam	15 days	Tue 6/10/25	Mon 7/7/25						
14	0%		JC	253309 - KVB Bridge Lightin	South Side Beam	15 days	Mon 7/14/25	Tue 8/5/25						
15	0%		JC	253309 - KVB Bridge Lightin	Pole Lights	10 days	Tue 6/10/25	Wed 6/25/25						
16	0%		JC	253309 - KVB Bridge Lightin	North Side Cable Lighting	15 days	Tue 6/10/25	Mon 7/7/25						
17	0%		JC	253309 - KVB Bridge Lightin	South Side Cable Lighting	15 days	Mon 7/14/25	Tue 8/5/25						
18	0%		JC	253309 - KVB Bridge Lightin	Relocate/Install Controls	20 days	Mon 6/16/25	Wed 7/16/25						
19	**0%**		**JC**	**253309 - KVB Bridge Lightir**	**Start Up & Commissioning**	**7 days**	**Mon 8/18/25**	**Fri 8/29/25**						
20	0%		JC	253309 - KVB Bridge Lightin	Addressing Fixtures	5 days	Tue 8/19/25	Wed 8/27/25						
21	0%		JC	253309 - KVB Bridge Lightin	Programing & Start Up	10 days	Tue 8/19/25	Thu 9/4/25						
22	0%		JC	253309 - KVB Bridge Lightin	Commissioning & Burn in	5 days	Tue 8/19/25	Wed 8/27/25						
23	0%		JC	253309 - KVB Bridge Lightin	Training & hand Over	2 days	Tue 8/19/25	Wed 8/20/25						
24	0%		JC	253309 - KVB Bridge Lightin	Warranty Documentation	1 day	Tue 8/19/25	Tue 8/19/25						
25														
26														
27	0%				Dates Not Available To Work									
28														
29	0%				AC/DC	1 day	Tue 5/20/25	Tue 5/20/25						
30	0%				CMA FEST	4 days	Wed 6/4/25	Mon 6/16/25						
31	0%				4th Of July	2 days	Thu 7/3/25	Mon 7/7/25						
32	0%				COLDPLAY	2 days	Tue 7/22/25	Wed 7/23/25						
33	0%				THE WEEKEND	2 days	Thu 6/12/25	Fri 6/13/25						
34	0%				TITANS REGULAR SEASON	2 days	Sat 8/9/25	Mon 8/11/25						
35	0%					2 days	Fri 8/15/25	Mon 8/18/25						
36	0%					2 days	Fri 8/22/25	Mon 8/25/25						
37	0%					2 days	Sun 9/7/25	Mon 9/8/25						

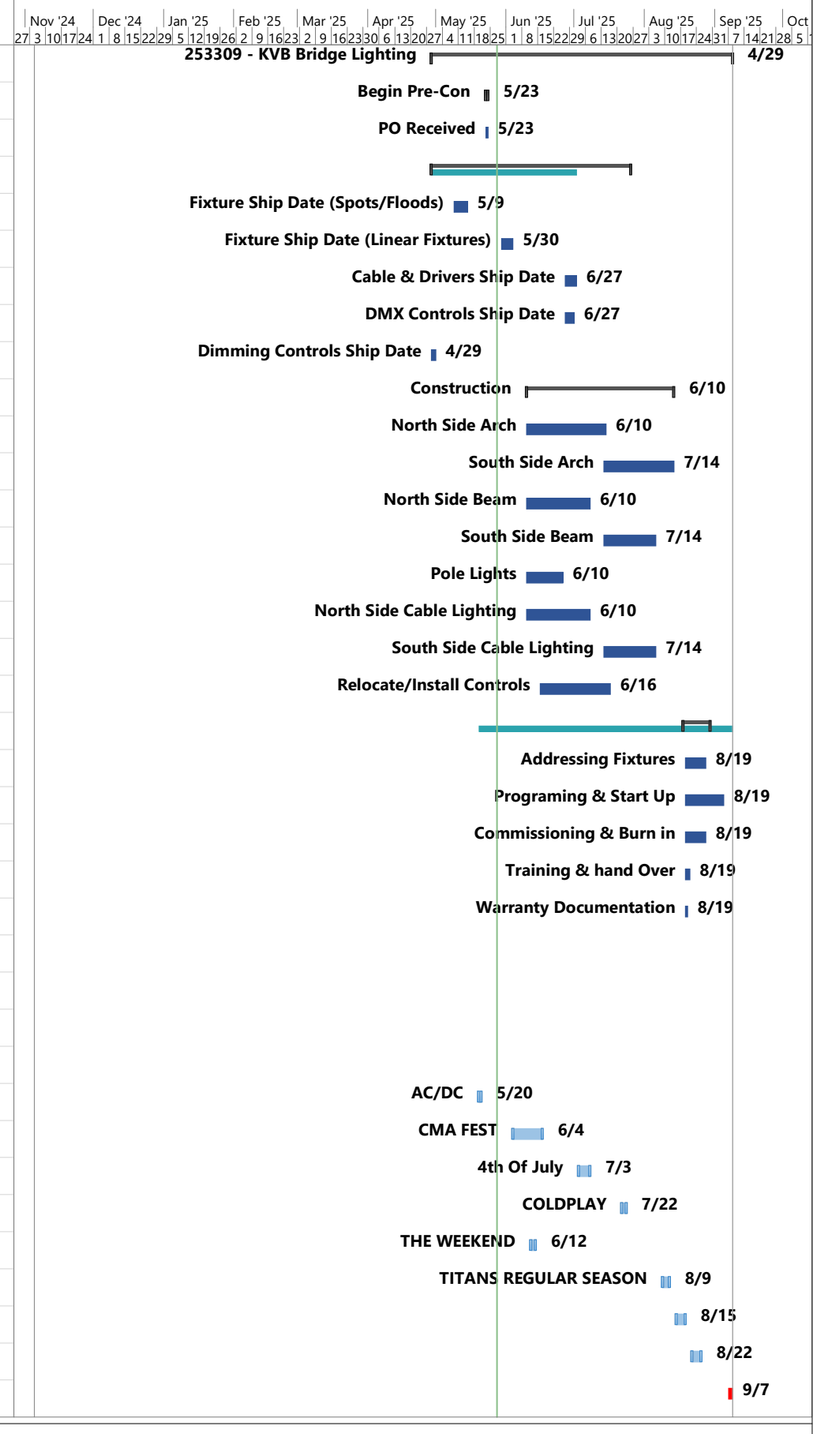

Project: KVB Bridge Lighting
Date: Wed 5/28/25

Task	Summary	Inactive Milestone	Duration-only	Start-only	External Milestone	Critical Split		
Split	Project Summary	Inactive Summary	Manual Summary Rollup	Finish-only	Deadline	Progress		
Milestone	Inactive Task	Manual Task	Manual Summary	External Tasks	Critical	Manual Progress		
